




TOWN OF QUEENSBURY
742 Bay Road, Queensbury, NY. 12804-5902

Jenkinsville Community Water Project Contract 1: Progress Report 8/31/26

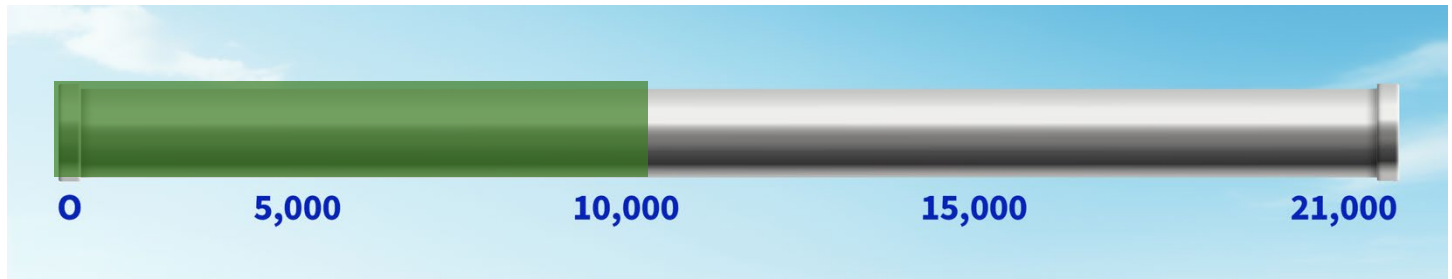

1. Construction Status:

- Construction on Contract 1 began July 14, 2026. Approximately 10,000 of a total of 21,000 linear feet of water main has been installed as have 125 long and short side services, as of August 27, 2026. Water main installation is complete on Mud Pond Road, Azure Drive and Rainbow Drive and about 80% complete on Jenkinsville Road. Water main installation will continue on Jenkinsville Road followed by Sunnyside Road East and Stonehurst Drive.



2. Status of Residential Water Connections:

- Zone 1 properties to be connected to Town water in Contract 2: 66 of 75.
- Zone 2: Properties wishing to connect to Town Water in Contract 2: 37 of 72.

3. Town Schedule:

- Contractor required to complete Phase 1 by end of May 2027. Based on progress thus far, work should be completed well within this deadline.
- Town to seek bids for Phase 2 work in 2027. Water service contract expected to be completed in 2027. Efforts being made to accelerate this schedule with a possible bid date in 2026. Material pre-purchase also being considered for some items that have longer lead times.
